Muz 34]

MUZRAI SECRETARIAT.

~~190~~ 1895-6

File No. 32

I

SUBJECT.

Sri Chamarajendra Sanskrit College, Bangalore

Transfer of the building known as the Lower Arsenal in Fort, Bangalore to the Muzrai Department for the use of the Bangalore Sanskrit College

Report to accompany the bill for repairing & improving Sanscrit School at Fort.

— " —

As the want of a suitable building to accomodate the Sanscrit College was much felt and as the Camp equipage building in the Fort appeared to be the best suited for the purpose if repaired, altered & added to, it was taken in hand with the approval of the Dewan & the following alterations & improvements were effected to render it in all ways suitable for the College.

The building as it stood was in a delapidated & Shaky Condition & an eyesore. The walls of the main structure were cracked in many places & at some points really dangerous. These portions were dismantled & rebuilt & the remainder of the walls made perfectly strong by bond stones.

Many of the Couples were completely decayed at their ends & in many of them the rafters were eaten up completely useless; the timber was also uniformely sagged, thus rendering the roof far from water tight. The tiles were removed, couples loosened uncoupled & after selecting such of the timbers as were

were found to be thoroughly sound were recoupled & fixed up & the roof completed with the old materials. The doors & windows were very much out of repair. These were thoroughly repaired & provided with bolts & locks & the windows with cross bars also

A no. of Cross walls were built dividing the building into Convenient rooms for the Classes.

In addition to the above improvements effected to the existing building a new line of rooms corresponding to those on the east was also built. For this extension such old wooden materials as was available was used up for the Couples & door & window frames; the remainder of the work being carried out with new materials.

In order to give the building a presentable appear-ance, pilasters, Cornice & ornamental ridging were provided.

The Small out house to the west was tho-roughly repaired & re-roofed & provided with Strong windows & doors.

The well in the premises which had no water in it for a long time was lowered till a depth of 6 ft of water was obtained & a pully was provided.

The ground was partly levelled, but as the work could not be satisfactorily done in the dry weather it was stopped to be resumed again in the rains.

The work carried out as per accompanying bill has been done satisfactorily.

H. W. Miller
Overseer.
12-6-95

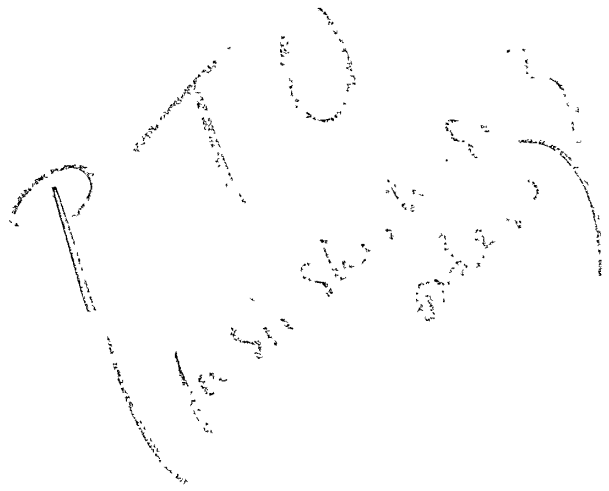

known as the Lower Arsenal in the Bangalore Fort

for the use of the Bang. Sanskrit College

Order

The transfer of the Building & the Museum buildings is sanctioned

repair at the Cost of Rs 5-5000 /

Rs 15000

This order is sanctioned — ~~The Museum Building Grant for 1895-96 will be increased by Rs 20000 as a Special~~

To meet the Cost of the repair of the Buildings

by: 3/7/95.

An additional Rs 5000/ is sanctioned & the Rs 15000 already sanctioned for repairs of Museum Buildings in the Budget for 1895-96.

1895-6.

Mwzrai.

Order No. 31-2

Dy Bangalore 3rd July 1895.

The transfer of the Building known as the Lower Arsenal in the Bangalore Fort to the Mwzrai Department for the use of the Bangalore Sanskrit College and its repair at the cost of Government for Rs 5,500 by that Department are sanctioned.

2. To meet the cost of the repair of the Building an addition of Rs 5000-- is sanctioned to the Rs 15000-- already sanctioned for repairs of Mwzrai Buildings, in Govt. Pro: No. 749 Mwz F 105-92 dated 25th February 1895 in the Budget for 1895-96.

Dewan's Order)

Secy.

To

The Comptroller, Mysore Govt.
Dy Commr Bangalore

Please see in sheet 6 in Dy Commr's order on the back of the Report below

To the same Lr No 644 dy 16-7-95

Memo.

Under the orders conveyed in Government Proceedings No. 31-2 dated 3rd. July 1895, the main building of the Chamarajendra Sanskrit College in Bangalore Fort has been thoroughly repaired at a cost of Rs 4198-13-6 and the College is now being held in the building.

2. Since, the following additional works to the cost of Rs 6261-2-6 have been executed in order to improve the general appearance of the College buildings.

Rs 2887-8-8. 1. An ornamental Compound wall 4 feet high all round on 3 sides to the total length of 1121 feet with stone and Chunam basement, dressed stone slab perforated work with pillars 20 feet apart and coping with stone slabs and brick in chunam on the top.

Rs 1709-3-10 2. A verandah in the front and the sides of the main building with dressed slab stone flooring and Mangalore tile roof supported on dressed stone pillars.

Rs 547-9-3 { 3 Converting the old Magazine into Students Quarters and making the necessary improvements.

Rs 944.13.9 { 4. Miscellaneous works - such as, levelling and forming the grounds in the College Compound, providing 2 teak-wood gates with iron bars for the main entrances, Constructing V shaped drain with stone slabs all along the verandah, Color washing, putting up Sun-shades etc.

Rs 171-15-0 { 5 Sundry repairs to the Sri Venkatramanaswami temple in the Fort, where the Veda classes of the College were being held - such as, providing new doors and windows and Color washing.

3. Thus, the total cost of the entire works in Connection with the College building has come up to Rs 10,460- Towards this, a sum of Rs 5500- has been sanctioned by Government in their Proceedings No: 31-2 dated 3rd July 1895

referred to above and provision is now requested to meet the balance, viz Rs 4,960.

4. The Abstract Measurement Lists of the works are herewith submitted and the rates have been duly checked by Mr. Y. Sreenivasa Rao, Executive Engineer of the Bangalore Division.

14-6-96

(P 7 6)

270

Rs 4960

To be met from the Mungeri Buildings Budget, which for 1896/97 may provide Rs 5000 in addn to Rs 15000 already sanctd.

16-6-96

1895-6

Murrai.

Read:—

Govt Reso no 31-2
of 3rd Jan 96 Sanctioning
the transfer of the
Building known as
the Lower Arsenal
in the Bangalore Fort
to the Mur. Dept
for the use of the
Bangalore Sanskrit
College, and its repairs
at a cost of Rs 5300
from Murrai Funds.

Read also.

Note by the Mur. Supt
of 14th June 1896 stating
that in addition to the
repairs sanctioned
under the above ord
of Govt, the Marquis
noted extra works have
been carried out, and
requesting provision

An ornamental Compound
wall
· Constructing a Verandah
in the front & the two sides
· Converting the Magazine
into Students Quarters.
Miscellaneous
works, such as Constructing
a V Shaped drain all along
the Verandah, levelling &
forming the ground in the

for the payment of the additional
outlay of Rs. 4960 incurred
for such extra works.

Order thereon. No. 1263 dt 18/6/96
Mun 732-95

~~To meet the cost of the extra works~~ accordingly.

To meet the further outlay of Rs 4960 on account of the extra works noted ~~in the Margin~~, an additional Rs 5000 is sanctioned to the ~~aforesaid~~ State Grant of Rs 15000, already sanctioned vide Govt Res No. 809 dt Mun 7105-92 3rd Feb 1896 for the repairs of Municipal Buildings during the year 1896-7.

2. The Comptroller will be requested to provide ~~for~~ the ~~further~~ sum of Rs 5000. herein sanctioned in the Mun. Budget for 1896-7

To the Comptroller

By order
Mun Secy
